

Bloomfield Truck Parking

DEVELOPMENT FEASIBILITY · CAPEX → COST PER STALL → NOI → DSCR

Bloomfield, CT · IOS truck parking
Test 1.25× DSCR at 65% LTC · Aug 2026

None of the three build scenarios can be financed.

The best covers 0.77× against a 1.25× test. This is not a marginal miss and not one pessimistic input — it holds across every reasonable flex of the assumptions.

0.77×


BEST-CASE DSCR

SCENARIOS

S1 · FULL ASPHALT, STAFFED \$43,283 10 ac · 216 stalls · 0.48×	S2 · VALUE-ENGINEERED \$34,882 10 ac · 216 stalls · 0.77×	S3 · RETROFIT PAVED YARD \$36,061 8 ac · 187 stalls · 0.73×
---	--	--


COST PER STALL AGAINST WHAT THE INCOME CAN CARRY

FIXED VS. VARIABLE CAPEXDASHED = CEILING AT 1.25× DSCR

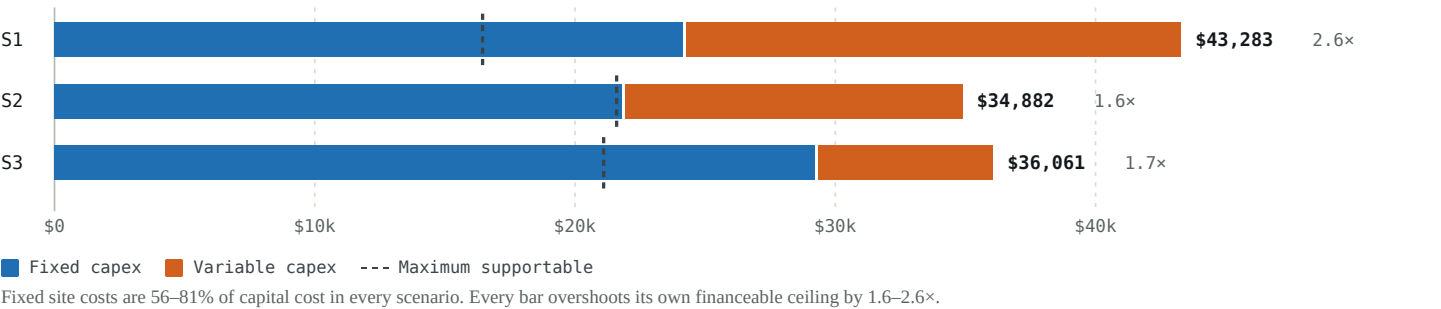


THE SINGLE RATIO THAT DECIDES IT

ALL-IN COST PER STALL ÷ NOI PER STALLMUST CLEAR 14.2×



A 1.25× DSCR at 65% LTC and an 8.674% mortgage constant requires a 7.05% yield on cost — so cost per stall can be no more than about 14.2× NOI per stall.

WHERE THE CAPITAL GOES

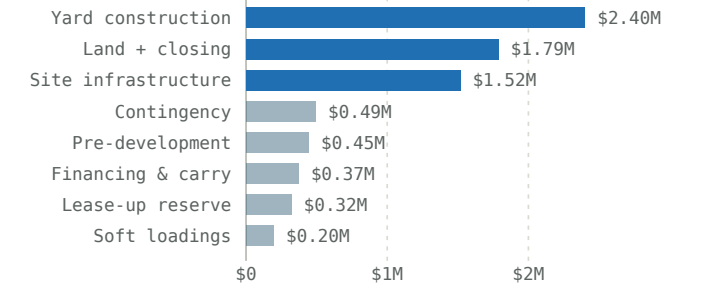

STABILIZED OPERATIONS · S2

Effective gross income	\$801,405
Operating expenses	(\$472,611)
Net operating income	\$328,793
Blended revenue / stall / mo	\$309
Opex / stall / mo	\$182
Margin / stall / mo	\$127
Yield on cost	4.36%
Debt yield	6.7%
Break-even occupancy	112.7%

\$127 per stall per month has to carry \$34,882 of capital. A break-even occupancy above 100% means full occupancy still does not cover debt service.

WHAT EACH SCENARIO WOULD NEED TO BE FINANCEABLE


	MODELLED RATE	REQUIRED RATE	GAP	MAX COST / STALL	MAX LAND \$/AC	BREAK-EVEN OCC.
S1 · full asphalt, staffed	\$353	\$520	+47.5%	\$16,448	(\$392,162)	132.2%
S2 · value-engineered	\$309	\$392	+26.7%	\$21,599	(\$105,726)	112.7%
S3 · retrofit paved yard	\$322	\$414	+28.9%	\$21,100	\$42,818	115.0%

Rates are blended revenue per stall per month. A negative maximum land price means the improvements alone cost more than the income can carry, so no land basis rescues those two. Only the retrofit leaves residual land value — \$42,818/acre against the \$385,000/acre assumed.

What moves the number


SCALE · SPECIFICATION · THE FINANCEABLE ENVELOPE

SCALE IS THE STRONGEST LEVER — BUT ONLY ABOVE ~14 ACRES

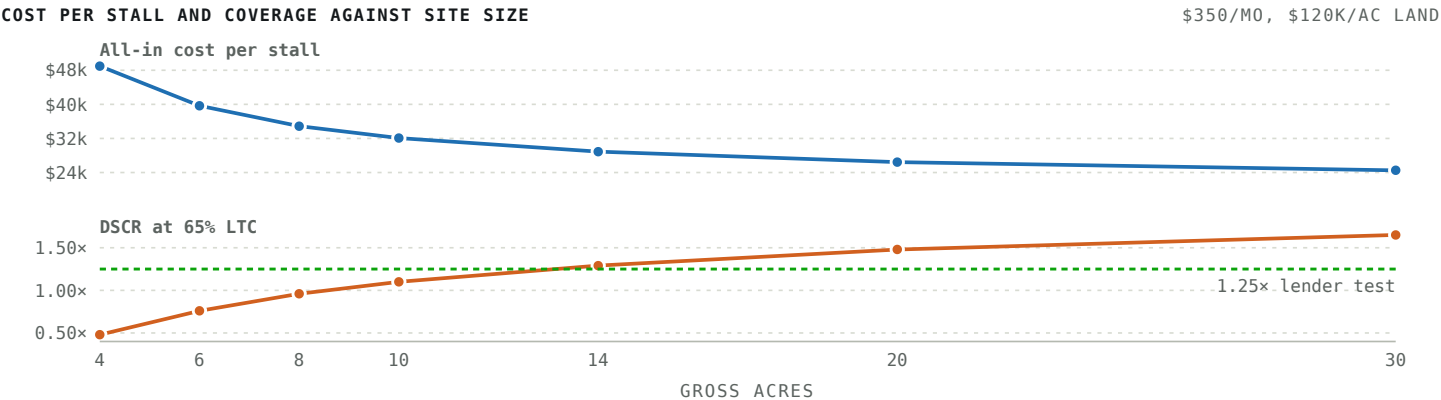

Fixed site costs spread across more stalls. The crossover through 1.25x happens between 10 and 14 acres; below 8 acres nothing else can rescue the deal.

WHY VOLUME BUYS SO LITTLE




THE FINANCEABLE ENVELOPE

\$/MO	\$0	\$40K	\$80K	\$120K	\$160K	\$200K
\$300	1.06	0.96	0.87	0.79	0.72	0.65
\$325	1.26	1.14	1.03	0.94	0.86	0.79
\$350	1.45	1.31	1.20	1.10	1.01	0.93
\$375	1.64	1.49	1.37	1.25	1.16	1.07
\$400	1.83	1.67	1.53	1.41	1.30	1.21
\$425	2.02	1.85	1.70	1.56	1.45	1.34

At the modelled \$315/month **no land price clears the test — not even free land.** Rate has to move first on a 10-acre programme.

SPECIFICATION — WHAT A DESIGN DECISION IS WORTH PER STALL

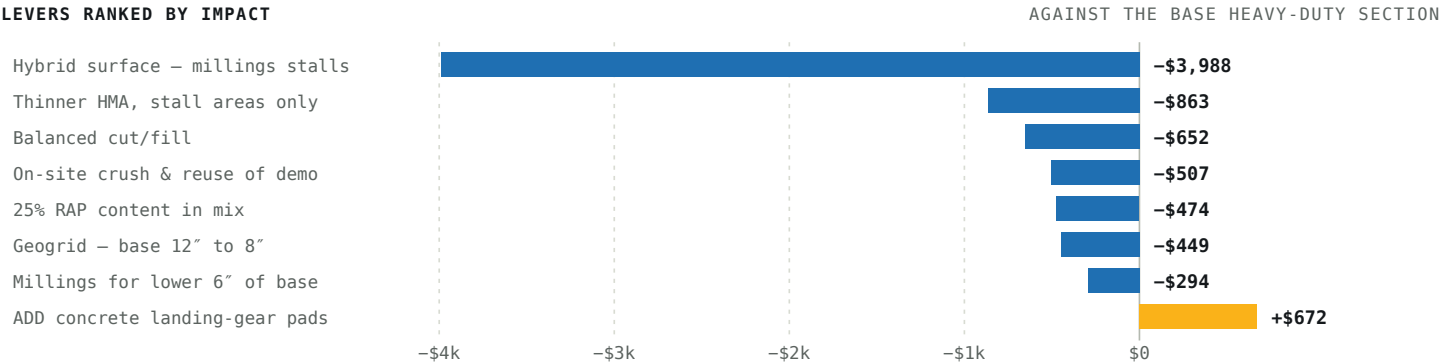

One lever is worth more than all the others combined. Stacked, the compatible levers take yard construction from \$13,702 to \$8,812 per stall — a 35.7% cut, three to five times what volume delivers.

RECOMMENDATION

Do not pursue a 10-acre greenfield build at \$175,000 per acre.

- Specify the hybrid section first.** Paved aisles with compacted millings stalls is worth \$3,988 per stall, costs nothing but a design decision, and shrinks the stormwater basin as a side effect.
- Then buy site size.** 14+ acres at or below \$120k/acre yielding 25+ stalls per gross acre is the only configuration that clears a lender's test on its own economics — 1.67x DSCR at 9.43% yield on cost.
- Spend the first two dollars on diligence, not land.** A rate survey of secured 53 ft stalls within 15 miles, and a zoning pre-application meeting with Bloomfield TPZ. Both are cheap and either can kill the deal before land is optioned.

Two caveats sit outside the model. The \$315–340/month rate is inferred from the national \$150–500 band, not an observed Bloomfield comp. And Bloomfield TPZ has treated outdoor storage as a use not permitted as a principal use — a text amendment or variance is likely required, not just site-plan approval.
